

TRAFFIC CONTROL PLAN NARRATIVE

FOLLOW THE CONSTRUCTION SEQUENCING, UNLESS OTHERWISE APPROVED. TWO WEEKS PRIOR TO CONSTRUCTION, PORTABLE CHANGEABLE MESSAGE SIGNS SHALL BE PLACED ON BOTH ENDS OF THE PROJECT.

BEFORE BEGINNING WORK, PLACE APPLICABLE SIGNAGE AND BARRICADES IN ACCORDANCE WITH TXDOT STANDARDS, TMUTCD, SW3P MEASURES, AND CITY OF AUSTIN STANDARDS.

ALL END CONDITIONS ARE TO BE TREATED TO MEET A 3:1 SAFETY SLOPE AFTER EACH WORKDAY.

CONTRACTOR TO CONDUCT CONSTRUCTION OPERATIONS SO AS TO PROVIDE THE LEAST POSSIBLE INTERFERENCE TO TRAFFIC AND TO PERMIT THE CONTINUOUS MOVEMENT OF TRAFFIC OR AS PERMITTED BY THE SEQUENCE OF CONSTRUCTION. PROVIDE SAFE AND CONVENIENT ACCESS TO ABUTTING PROPERTY AT ALL TIMES. PUBLIC SAFETY SHALL BE THE HIGHEST PRIORITY AT ALL TIMES. FURNISH ALL TRAFFIC CONTROL EQUIPMENT AND MAINTAIN IN A SATISFACTORY CONDITION THROUGHOUT THE CONSTRUCTION. DO NOT BEGIN OR SHUT DOWN OPERATIONS UNTIL PROPER COORDINATION IS COMPLETE.

PHASE 1

1. SET-UP TRAFFIC CONTROL DEVICES IN ACCORDANCE WITH TXDOT STANDARDS, TMUTCD, AND CITY OF AUSTIN STANDARDS. INSTALL ADVANCE WARNING SIGNS PER TXDOT STANDARD DETAILS.
2. INSTALL SW3P.
3. CONSTRUCT PROPOSED STORM SEWER AS SHOWN ON LAYOUTS OUTSIDE OF EXISTING ROADWAY.
4. CONSTRUCT PROPOSED TRAFFIC SIGNAL CONDUITS, FOUNDATION, AND SIGNAL POLES AS SHOWN ON LAYOUTS. CONTRACTOR TO COORDINATE WITH ENERGY COMPANY FOR ANY DE-ENERGIZING NEEDED FOR CONSTRUCTION.

PHASE 2

1. SET-UP TRAFFIC CONTROL DEVICES IN ACCORDANCE WITH TXDOT STANDARDS, TMUTCD, AND TCP DETOUR LAYOUTS. THE WORK PERFORMED IN PHASE 2 IS ONLY TO BE CONSTRUCTED DURING USING CLOSURES. CLOSE THE INTERSECTION OF OLD SAN ANTONIO ROAD AND PURYEAR ROAD.
2. CLOSE OLD SAN ANTONIO ROAD AND PURYEAR ROAD FOR PROPOSED LIMITS OF WORK AND AS SHOWN ON DETOUR LAYOUTS.
3. BEGIN REMOVALS OF EXISTING SIDEWALKS, STRIPING, CULVERTS, AND OTHER ELEMENTS AS SHOWN IN REMOVAL LAYOUTS.
4. BEGIN PROPOSED ROADWAY WORK ON OLD SAN ANTONIO ROAD AND PURYEAR ROAD AS SHOWN ON ROADWAY LAYOUTS. CONTRACTOR TO WORK ON BOTH ROADWAY CONCURRENTLY TO EXPEDITE THE CONSTRUCTION TIMELINE.
5. INSTALL PROPOSED SIGNAL MAST ARMS AND SIGNAL HEADS AS SHOWN IN LAYOUTS. PERFORM SIGNAL WIRING AS SHOWN IN PLANS AND AS NEEDED TO MAKE SIGNAL OPERATIONAL.
6. INSTALL PROPOSED SIDEWALKS, RAMPS, AND FLATWORK AS SHOWN IN LAYOUTS.

PHASE 3


1. INSTALL PERMANENT STRIPING AND SIGNING AS SHOWN IN PLANS AND IN ACCORDANCE WITH TXDOT STANDARDS.
2. INSTALL TOPSOIL AND SEEDING.
3. PERFORM PROJECT CLEAN-UP.

NOTES:

1. FOR ANY PEDESTRIAN TRAFFIC, CONTRACTOR TO PROVIDE A PEDESTRIAN ESCORT DURING CONSTRUCTION HOURS.
2. CONTRACTOR TO PRIORITIZE THE SAFETY OF THE TRAVELING PUBLIC AT ALL TIME. ALL OPEN PITS SHALL BE COVERED BY AN APPROPRIATE METHOD AND SAFETY SLOPES SHALL BE 3:1 OR FLATTER DURING ALL NON-WORKING HOURS.

NO.	DATE	REVISION	APPROVAL
			
Westwood			
Phone (210) 265-8300 211 N Loop 1604 E Suite 205 Toll Free (888) 937-5150 San Antonio, TX 78232 westwoodps.com			
Westwood Professional Services, Inc. TPE FIRM REGISTRATION NO. 7-11726 TPELS FIRM REGISTRATION NO. 10074301			
OSR AT PURYEAR			
Sequence of Constructon			
PROJ. NO. 00-000	FEDERAL AID PROJECT		HIGHWAY
			XXXXX
STATE	DISTRICT	COUNTY	SHEET NO.
TEXAS	XXX	XXXXX	13
CONTROL	SECTION	JOB	
XXXX	XX	XXX	

9/26/17 AM
C:\Users\westwood\OneDrive\Documents\1450058-TCB-DETOUR-LAY-01.dwg

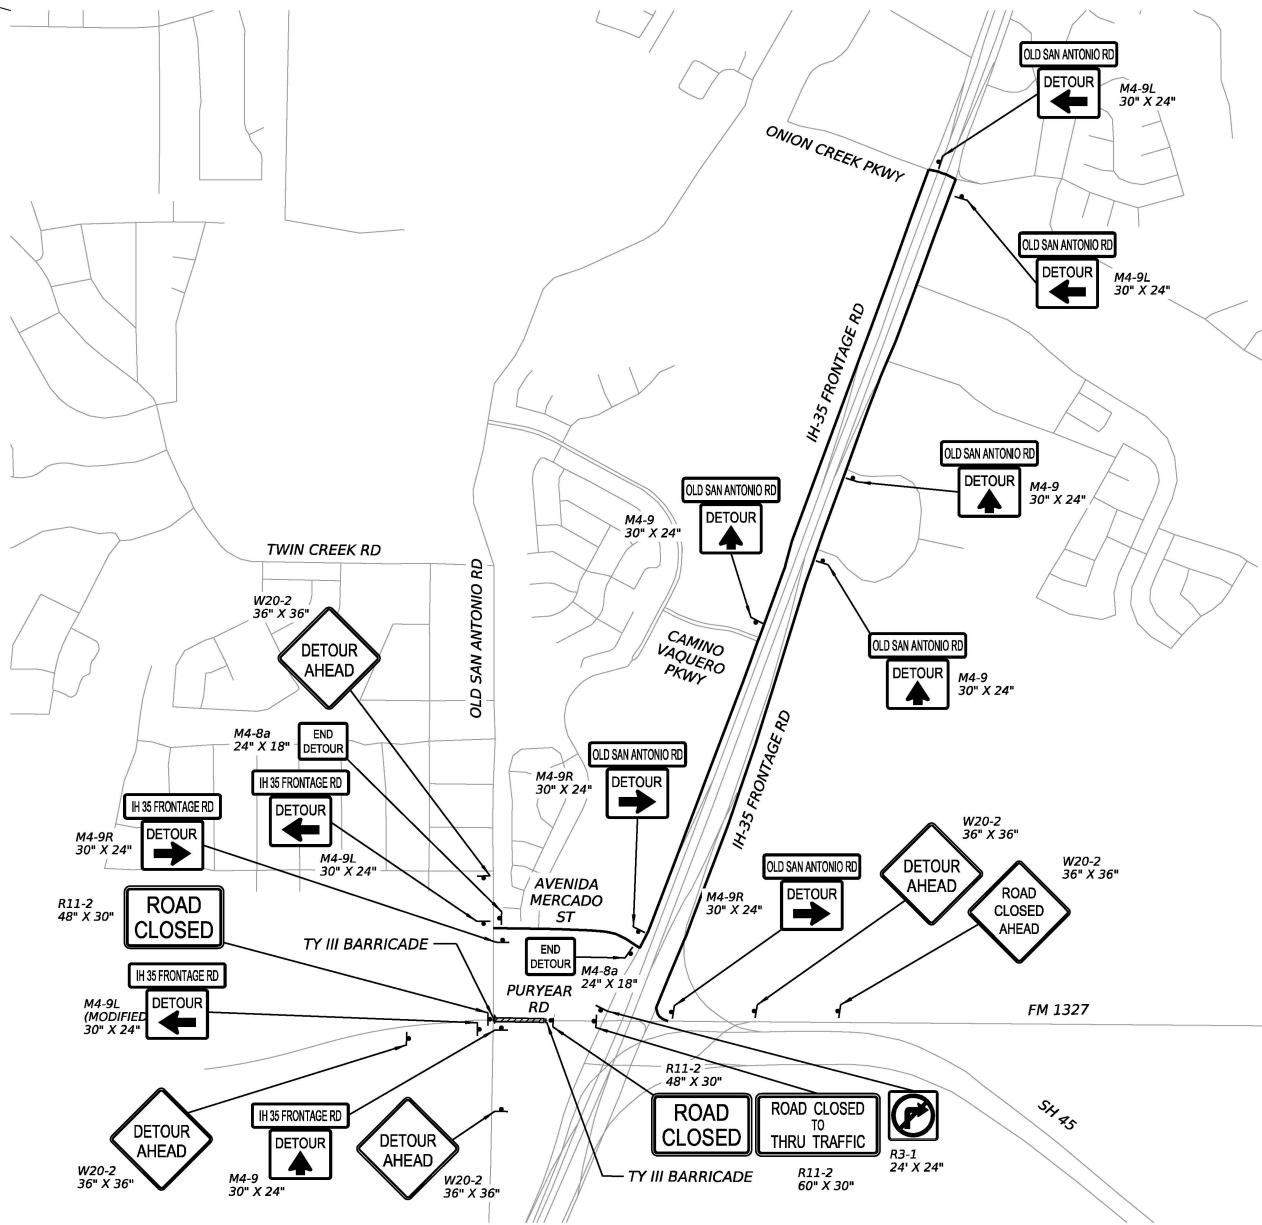

LEGEND


- EXISTING ROADWAY
- PROPOSED DETOUR ROUTE
- WORKZONE
- SIGN
- TY III BARRICADE

NOTES:

- FOR ANY PEDESTRIAN TRAFFIC, CONTRACTOR TO PROVIDE A PEDESTRIAN ESCORT DURING CONSTRUCTION HOURS.

NO.				DATE	REVISION	APPROVED
N.T.S						
Westwood Phone (210) 265-8300 211 N Loop 1604 E Suite 205 Toll Free (888) 937-5150 San Antonio, TX 78232 westwoodps.com Westwood Professional Services, Inc. TSP# FIRM REGISTRATION NO. 1-11755 TSP# FIRM REGISTRATION NO. 10074391						
OSR AT PURYEAR						
DETOUR LAYOUT PHASE 02						
FED. AID PROJ. NO.		FEDERAL AID PROJECT		HIGHWAY		
				XXXX		
STATE		DISTRICT		COUNTY		SHEET NO.
TEXAS		AUS		COUNTY		14
CONTROL		SECTION		JOB		
XXXX		XX		XXX		

9/16/2025 AM
C:\Users\westwood\OneDrive\Documents\14501058-TCE-DETOUR-LAY-02.dwg

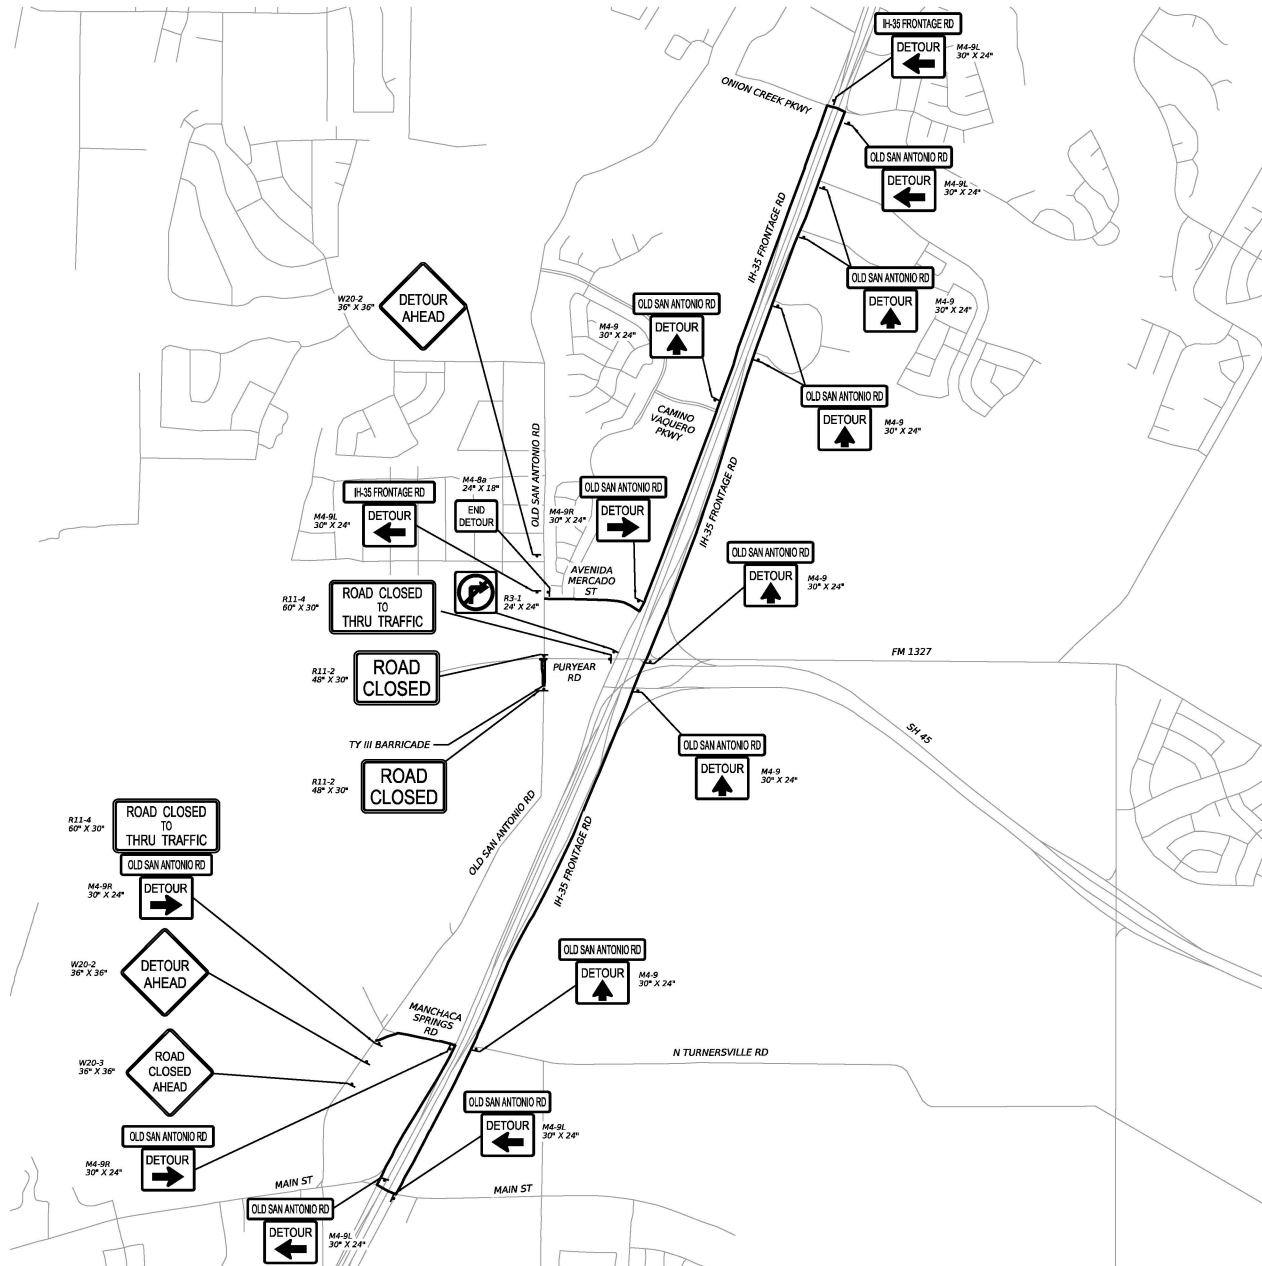

LEGEND

- EXISTING ROADWAY
- PROPOSED DETOUR ROUTE
- WORKZONE
- SIGN
- TY III BARRICADE

NOTES:

1. FOR ANY PEDESTRIAN TRAFFIC, CONTRACTOR TO PROVIDE A PEDESTRIAN ESCORT DURING CONSTRUCTION HOURS.

NO. DATE REVISION APPROVED			
N.T.S			
Westwood Phone (210) 265-8300 211 N Loop 1604 E Suite 205 Toll Free (888) 937-5150 San Antonio, TX 78232 westwoodps.com Westwood Professional Services, Inc. TDEC FIRM REGISTRATION NO. 1-11755 TBDPLS FIRM REGISTRATION NO. 10074301			
OSR AT PURYEAR			
DETOUR LAYOUT PHASE 02			
FED. AID PROJ. NO.	FEDERAL AID PROJECT		HIGHWAY
STATE	DISTRICT	COUNTY	XXXX
TEXAS	AUS	COUNTY	SHEET NO.
CONTROL	SECTION	JOB	15
XXXX	XX	XXX	
